HAZEL GREEN HS WRESTLING + FLAG FOOTBALL

New metal training building — PROPOSAL SET REV B

Replaces the old 55' x 45' wrestling room (10' ceiling) at Hazel Green High School, 14380 Hwy 231-431 N, Hazel Green, AL 35750 (Madison County Schools property; location on campus TBD). Supplier: Summertown Metals, 3864 Summertown Hwy, Summertown, TN 38483, (931) 796-1521 (quote TBD).

SHEET INDEX

P1-G-101	Cover + code summary — Rev B (Rev A superseded)
P1-A-201	Floor plan — Rev B (Rev A superseded)
P1-A-301	Elevations + section — Rev B (Rev A superseded)
P1-A-901	3D massing — Rev B (Rev A superseded)

PROJECT DATA (ASSUMED unless cited)

- Building 60' x 125' = 7,500 SF, 1 storey, clear span, 5 x 25' bays, eave 16', 14' min clear, 1:12 gable.
- D-095 (Shane 2026-10-15 5:12 AM CT) supersedes the D-094 layout: restrooms off the corridor; boys wrestling locker room added (ASSUMED — confirm wording); each locker room has its own showers.
- Rooms: wrestling mat room 3,000 SF (42' x 42' mat) · girls' flag football locker 832 SF · boys wrestling locker 832 SF · 2 team shower / WC rooms 364 SF each · women's + men's restrooms 260 SF each · coaches' office 286 SF · storage 143 SF · JAN. / mech 143 SF · 8' N-S + E-W corridors.
- Remodel set (P1-G-001 Rev E, P1-A-101 Rev C, P1-G-002 Rev B) stays the base option.
- Cost: TBD per the Summertown Metals quote + site, foundation, MEP, permit, design. No prices invented.
- Contact: Shane Brazelton, 256-508-4608, brazeltonshane@gmail.com.

CODE SUMMARY — IBC / IPC 2021 (AHJ to confirm)

- Occupancy: A-3 (indoor athletics / training), accessory to Group E campus (ASSUMED).
- Construction: Type IIB (non-combustible PEMB) (ASSUMED).
- Area: A-3 IIB non-sprinklered 9,500 SF / 1 storey allowed (Table 506.2) vs 7,500 SF: PASS.
- Sprinklers: Not required if fire area <= 12,000 SF and load < 300 (903.2.1.3); AHJ / Madison County Schools may require.

OCCUPANT LOAD (IBC 2021 Table 1004.5)

Wrestling mat room	3,000 SF / 50	60
Girls Flag Football Locker Room	832 SF / 50	17
Coaches' Office	286 SF / 150	2
Boys Wrestling Locker Room	832 SF / 50	17
Storage	143 SF / 300	1
Jan. / Mech	143 SF / 300	1
TOTAL (restrooms / showers / corridors accessory)		**98**

EGRESS

- Width: 98 x 0.2 in = 19.6 in needed (1005.3.2) vs 288 in of exit doors (D1-D5): PASS.
- Mat room 60 occ. > 49: 2 exits needed (1006.2.1); 3 provided (D3, D4, corridor I1): PASS. Each locker room 17 occ.: 1 door to the corridor, then 2 directions.
- Travel (Table 1017.2, 200 ft non-sprinklered): worst 94 ft (boys locker far corner to D1, routes ASSUMED): PASS.
- Common path (Table 1006.2.1, 75 ft): worst 52 ft (boys locker far corner to the corridor (2 ways)): PASS.
- Exit doors: panic hardware (1010.2.9); exit signs + egress lighting (1008, 1013).

PLUMBING FIXTURES — IPC 2021 Table 2902.1

Basis: IPC 2021 Table 2902.1 occupancy A-3 (indoor sport facility) ASSUMED; 50 / 50 sex split of the building load (ASSUMED). 98 occ. -> 49 F + 49 M.

FIXTURE	RATIO	REQ.	PROVIDED
WC — female	1:40	2	3 (2 RR + 1 team) PASS
WC — male	1:75	1	2 + 1 UR PASS
Lavatory F / M	1:150 / 1:200	1 / 1	3 / 2 PASS
Drinking fountain	1:1000	1	2 (hi-lo) PASS
Service sink	1	1	1 (JAN.) PASS
Showers	not req. (A-3)	0	8 (4 + 4, 2 acc.) PASS


D-095: every restroom and both team shower / WC rooms have a door on the corridor; the women's / men's restrooms serve the public and visiting teams without entering a locker room.

OPEN ITEMS / FINDINGS

- CONFIRM: second locker room = boys wrestling (ASSUMED from 'boys lockeroom and boys locker room for wrestling'). If Shane meant a separate boys locker room too, a 3rd room needs another bay (60' x 150').
- Team / rosters: girls' flag football 30 + boys wrestling 30 ASSUMED.
- Size 60' x 125' (grown from 60' x 100'): Shane to confirm.
- Location on campus, utilities (water / sewer), geotech: TBD with Madison County Schools.
- Sprinklers / fire alarm: AHJ + district. Supplier quote: Summertown Metals (kit only).

PRELIMINARY — CONCEPTUAL DESIGN — NOT FOR CONSTRUCTION

PROJECT	PHASE	SHEET TITLE	SCALE	DATE	REV	DRAWN BY	SHEET
Hazel Green Regional Athletic Complex **Hazel Green HS · Phase 1 alternate: new metal training building**	**PHASE 1 ALTERNATE**	**COVER + CODE SUMMARY METAL BUILDING (ALT.)**	**NTS**	**October 2026**	**B**	Drawn by KEYSTONE (AI) for Shane Brazelton	**P1-G-101**

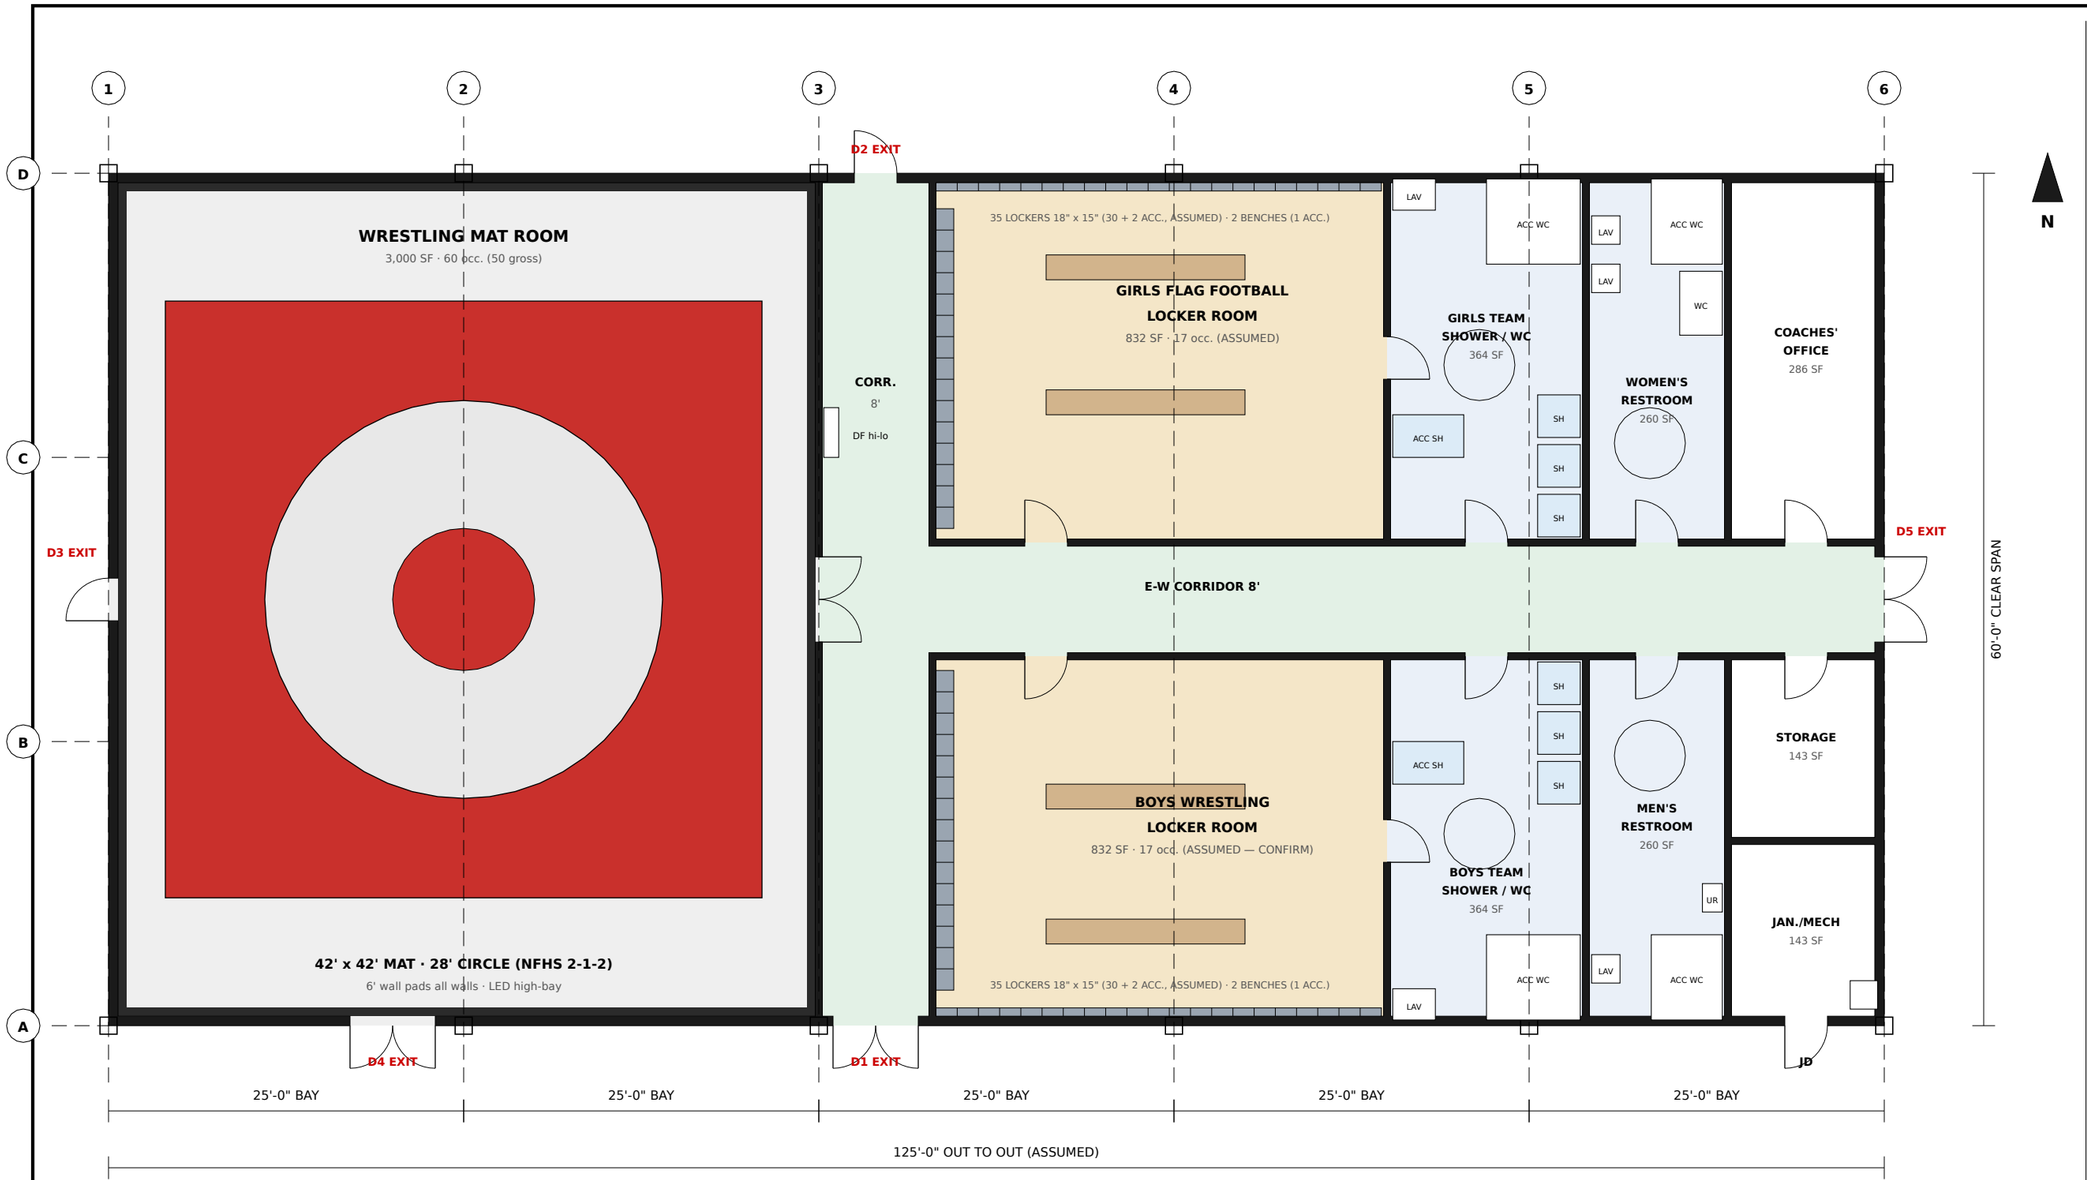

FLOOR PLAN — NEW METAL TRAINING BUILDING (ALTERNATE) REV B

3/32" = 1'-0" · 125' x 60' = 7,500 SF clear-span PEMB, 5 x 25' bays (ASSUMED) · plan north up · D-095

PLAN NOTES


- D-095 (Shane 2026-10-15 5:12 AM CT) supersedes the D-094 layout: restrooms open off the corridor; 2 locker rooms, each with its own showers.
- Grown one 25' bay: 60' x 100' -> 60' x 125' (ASSUMED). Mat room unchanged: 42' x 42' mat, 6' pads.
- North: girls' flag football locker room (ASSUMED). South: boys wrestling locker room (ASSUMED — CONFIRM: Shane wrote 'boys lockeroom and boys locker room for wrestling').
- Team shower / WC rooms: doors from the locker room AND the E-W corridor. Women's + men's restrooms open only off the corridor.
- Privacy vestibules / door hardware at the corridor doors TBD (architect).
- Exits (red): D1 main pair, D2 N, D3 W, D4 mat pair, D5 E corridor pair. Checks: P1-G-101.
- Wet walls TBD (CMU or moisture-resistant). Cost TBD per the Summertown Metals quote.

LEGEND


- wrestling mat
- 6' wall pads
- locker rooms
- showers / restrooms
- corridors
- lockers

PRELIMINARY — CONCEPTUAL DESIGN — NOT FOR CONSTRUCTION


PROJECT	PHASE	SHEET TITLE	SCALE	DATE	REV	DRAWN BY	SHEET
Hazel Green Regional Athletic Complex **Hazel Green HS · Phase 1 alternate: new metal training building**	**PHASE 1 ALTERNATE**	**FLOOR PLAN** **METAL BUILDING (ALT.)**	**3/32" = 1'-0"**	**October 2026**	**B**	Drawn by KEYSTONE (AI) for Shane Brazelton	**P1-A-201**




SOUTH ELEVATION (MAIN ENTRY) — 1/16" = 1'-0"




EAST ELEVATION (LOCKER END) — 1/16" = 1'-0"



NORTH ELEVATION — 1/16" = 1'-0"



WEST ELEVATION (MAT ROOM END) — 1/16" = 1'-0"

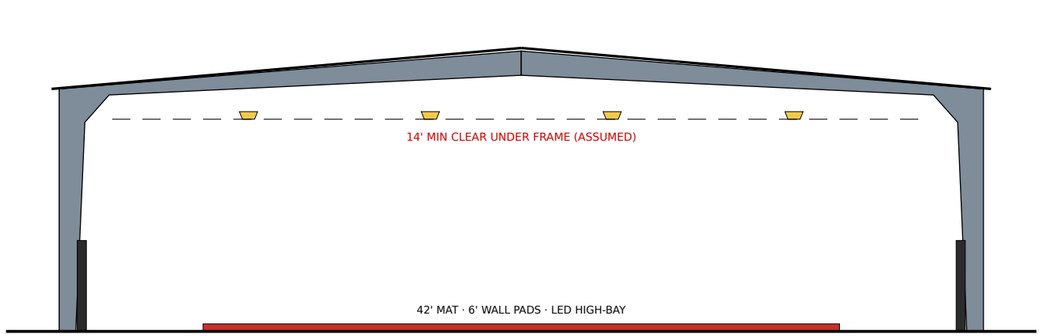

SECTION A-A THROUGH THE MAT ROOM (looking west) — 1/10" = 1'-0"

NOTES


- Pre-engineered clear-span rigid frame, 1:12 gable (ASSUMED). Eave 16' (ASSUMED), ridge 18.50' computed from the pitch. Final frame, eave and clear height by Summertown Metals' engineer.
- Walls / roof: insulated metal panels (IMP or metal + liner, Summertown kit), R-values per the Alabama Energy Code (IECC 2015 / 90.1-2013) — TBD by supplier (R-028.4).
- Daylight: translucent wall-panel band 12'-14' (ASSUMED) on all faces; skylights only where code / supplier allow (D-093 direction). LED high-bay in the mat room; LED elsewhere.
- Color: crimson wainscot 0-3' (school color, ASSUMED); light gray panels; dark roof (ASSUMED). Gutters / downspouts to rain capture if the campus wants it (unsized).
- Doors: hollow-metal exit doors with panic hardware on D1-D5 (Group A, IBC 1010.2.9); D5 = east corridor pair; JD = JAN. / mech service door (not an exit). Red tags = exits. D-095 Rev B: 60' x 125', 5 bays (ASSUMED).
- Foundation: slab-on-grade with column piers / anchor bolts per the PEMB reactions — geotech + structural TBD. No site plan yet (location on campus TBD).

PRELIMINARY — CONCEPTUAL DESIGN — NOT FOR CONSTRUCTION


PROJECT	PHASE	SHEET TITLE	SCALE	DATE	REV	DRAWN BY	SHEET
Hazel Green Regional Athletic Complex **Hazel Green HS · Phase 1 alternate: new metal training building**	**PHASE 1 ALTERNATE**	**ELEVATIONS + SECTION METAL BUILDING (ALT.)**	**1/16" = 1'-0"**	**October 2026**	**B**	Drawn by KEYSTONE (AI) for Shane Brazelton	**P1-A-301**

V1 AERIAL FROM THE SOUTHEAST (main entry + locker end)

isometric · not to scale · massing only

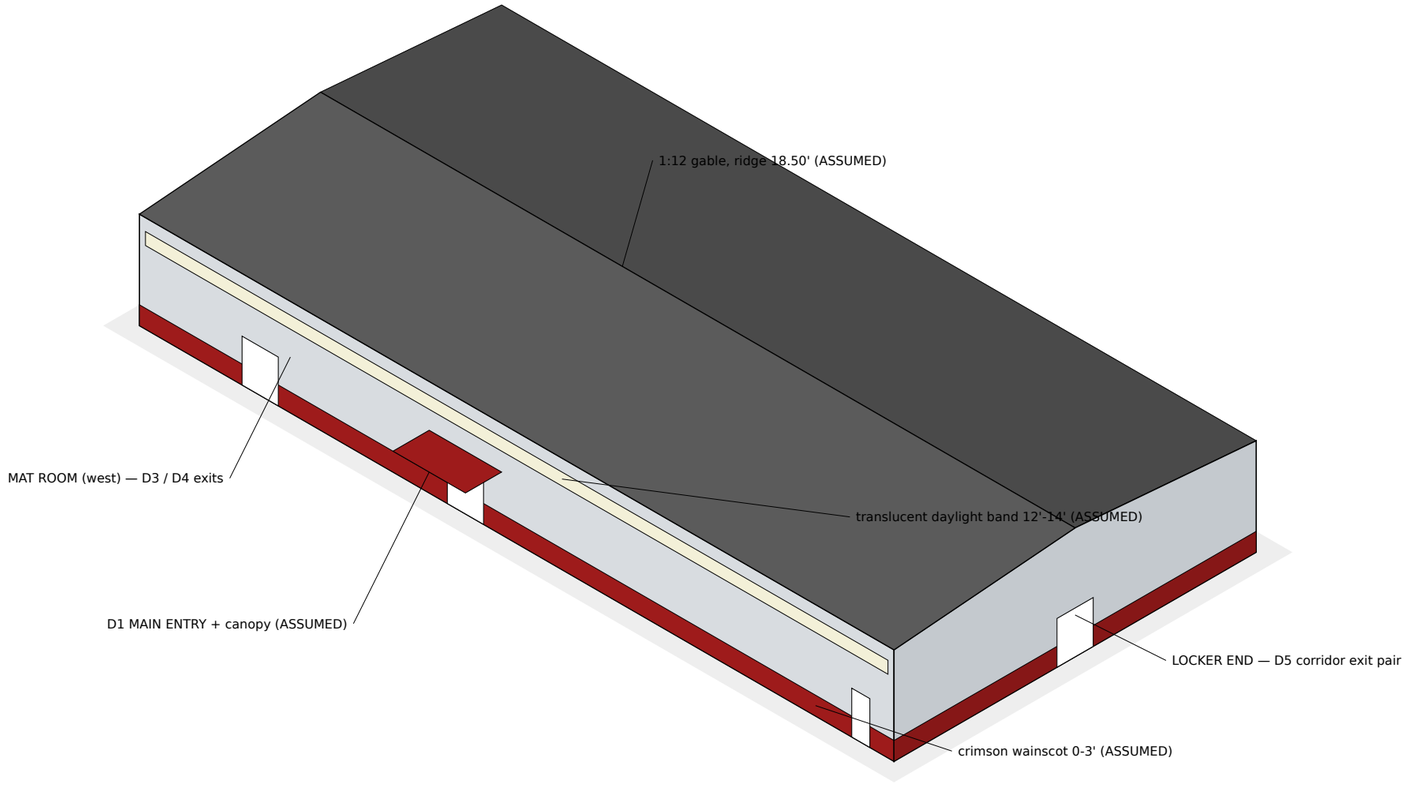

V2 FROM THE NORTHWEST (mat room end, D2 / D3)

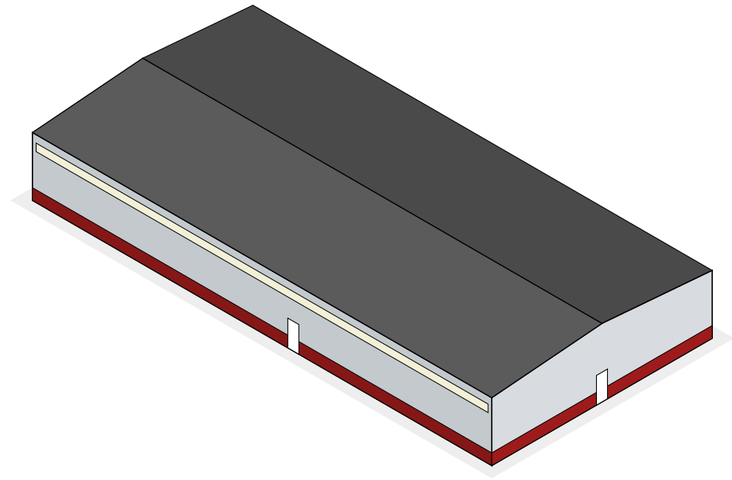

NOTES

- Massing only: 125' x 60' x 16' eave pre-engineered metal building (ASSUMED sizes, D-095 Rev B) from params/phase1_metal_bldg_rev_b.yaml.
- Summertown Metals kit (frame, panels, trim, doors). Colors, canopy and daylight band ASSUMED for discussion.
- Not modelled: site, grading, walks, parking, MEP units, gutters. Location on the HGHS campus TBD with Madison County Schools.
- Cost TBD per the supplier quote (no prices in this set).

PRELIMINARY — CONCEPTUAL DESIGN — NOT FOR CONSTRUCTION

PROJECT	PHASE	SHEET TITLE	SCALE	DATE	REV	DRAWN BY	SHEET
Hazel Green Regional Athletic Complex **Hazel Green HS · Phase 1 alternate: new metal training building**	**PHASE 1 ALTERNATE**	**3D MASSING** **METAL BUILDING (ALT.)**	**NTS**	**October 2026**	**B**	Drawn by KEYSTONE (AI) for Shane Brazelton	**P1-A-901**
