HAZEL GREEN HS WRESTLING + FLAG FOOTBALL

New metal training building — PROPOSAL SET REV A

Replaces the old 55' x 45' wrestling room (10' ceiling) at Hazel Green High School, 14380 Hwy 231-431 N, Hazel Green, AL 35750 (Madison County Schools property; location on campus TBD). Supplier: Summertown Metals, 3864 Summertown Hwy, Summertown, TN 38483, (931) 796-1521 (quote TBD).

SHEET INDEX

P1-G-101	Cover + code summary — Rev A
P1-A-201	Floor plan — Rev A
P1-A-301	Elevations + section — Rev A
P1-A-901	3D massing — Rev A

PROJECT DATA (ASSUMED unless cited)

- Building 100' x 60' = 6,000 SF, 1 storey, clear span, 4 x 25' bays, eave 16', 14' min clear, 1:12 gable.
- West: wrestling mat room 3,000 SF, one 42' x 42' mat. East: girls' flag football locker room 1,388 SF + toilet / shower, coach office, storage, JAN. / mech, corridor.
- D-094 (Shane 2026-10-14 9:52 PM CT): proposal set for the new building; the remodel (P1-G-001 Rev E, P1-A-101 Rev C, P1-G-002 Rev B) stays the base option.
- Cost: TBD per the Summertown Metals quote + site, foundation, MEP, permit, design. No prices invented. Companion text proposal (Shane, 2026-10-14) carries the remodel figures.
- Contact: Shane Brazelton, 256-508-4608, brazeltonshane@gmail.com.

CODE SUMMARY — IBC / IPC 2021 (AHJ to confirm)

- Occupancy: A-3 (indoor athletics / training), accessory to Group E campus (ASSUMED).
- Construction: Type IIB (non-combustible PEMB) (ASSUMED).
- Area: A-3 IIB non-sprinklered 9,500 SF / 1 storey allowed (Table 506.2) vs 6,000 SF: PASS.
- Sprinklers: Not required if fire area <= 12,000 SF and load < 300 (903.2.1.3); AHJ / Madison County Schools may require.

OCCUPANT LOAD (IBC 2021 Table 1004.5)

Wrestling mat room	3,000 SF / 50	60
Flag football locker room	1,388 SF / 50	28
Coach Office	196 SF / 150	2
Jan. / Mech	112 SF / 300	1
Storage	280 SF / 300	1
TOTAL (toilets / corridor accessory)		**92**

EGRESS

- Width: 92 x 0.2 in = 18.4 in needed (1005.3.2) vs 252 in of exit doors (D1-D5): PASS.
- Mat room 60 occ. > 49: 2 exits needed (1006.2.1); 3 provided (D3, D4, corridor): PASS. Locker room 28 occ.: 1 needed, D5 + corridor.
- Travel (Table 1017.2, 200 ft non-sprinklered): worst 74 ft (toilet / shower far corner to D5, routes ASSUMED): PASS.
- Exit doors: panic hardware (1010.2.9); exit signs + egress lighting (1008, 1013).

PLUMBING FIXTURES — IPC 2021 Table 2902.1

Basis: IPC 2021 Table 2902.1 occupancy A-3 (indoor sport facility) ASSUMED; 50 / 50 sex split of the building load (ASSUMED). 92 occ. -> 46 F + 46 M.

FIXTURE	RATIO	REQ.	PROVIDED
WC — female	1:40	2	3 (1 acc.) PASS
WC — male	1:75	1	1 single-user* PASS
Lavatory	1:150 F / 1:200 M	2	3 PASS
Drinking fountain	1:1000	1	2 (hi-lo) PASS
Service sink	1	1	1 (JAN.) PASS
Showers	not required (A-3)	0	4 (1 acc. roll-in) PASS


* single-user all-gender accessible toilet counted toward the male fixtures (IPC 2902.1.2) — AHJ to confirm. Boys' wrestling uses the existing HGHS locker rooms (ASSUMED).

OPEN ITEMS / FINDINGS

- Size 60' x 100' vs the 60' x 80' alternate: Shane to confirm (80' shrinks the locker side to 30').
- Team: girls' flag football + roster 30 ASSUMED; confirm with HGHS athletics.
- Location on campus, utilities (water / sewer for showers), geotech: TBD with Madison County Schools.
- Sprinklers / fire alarm: AHJ + district policy. Energy code envelope: supplier.
- Supplier quote: Summertown Metals (kit only); everything else TBD.

PRELIMINARY — CONCEPTUAL DESIGN — NOT FOR CONSTRUCTION

PROJECT	PHASE	SHEET TITLE	SCALE	DATE	REV	DRAWN BY	SHEET
Hazel Green Regional Athletic Complex **Hazel Green HS · Phase 1 alternate: new metal training building**	**PHASE 1 ALTERNATE**	**COVER + CODE SUMMARY METAL BUILDING (ALT.)**	**NTS**	**October 2026**	**A**	Drawn by KEYSTONE (AI) for Shane Brazelton	**P1-G-101**

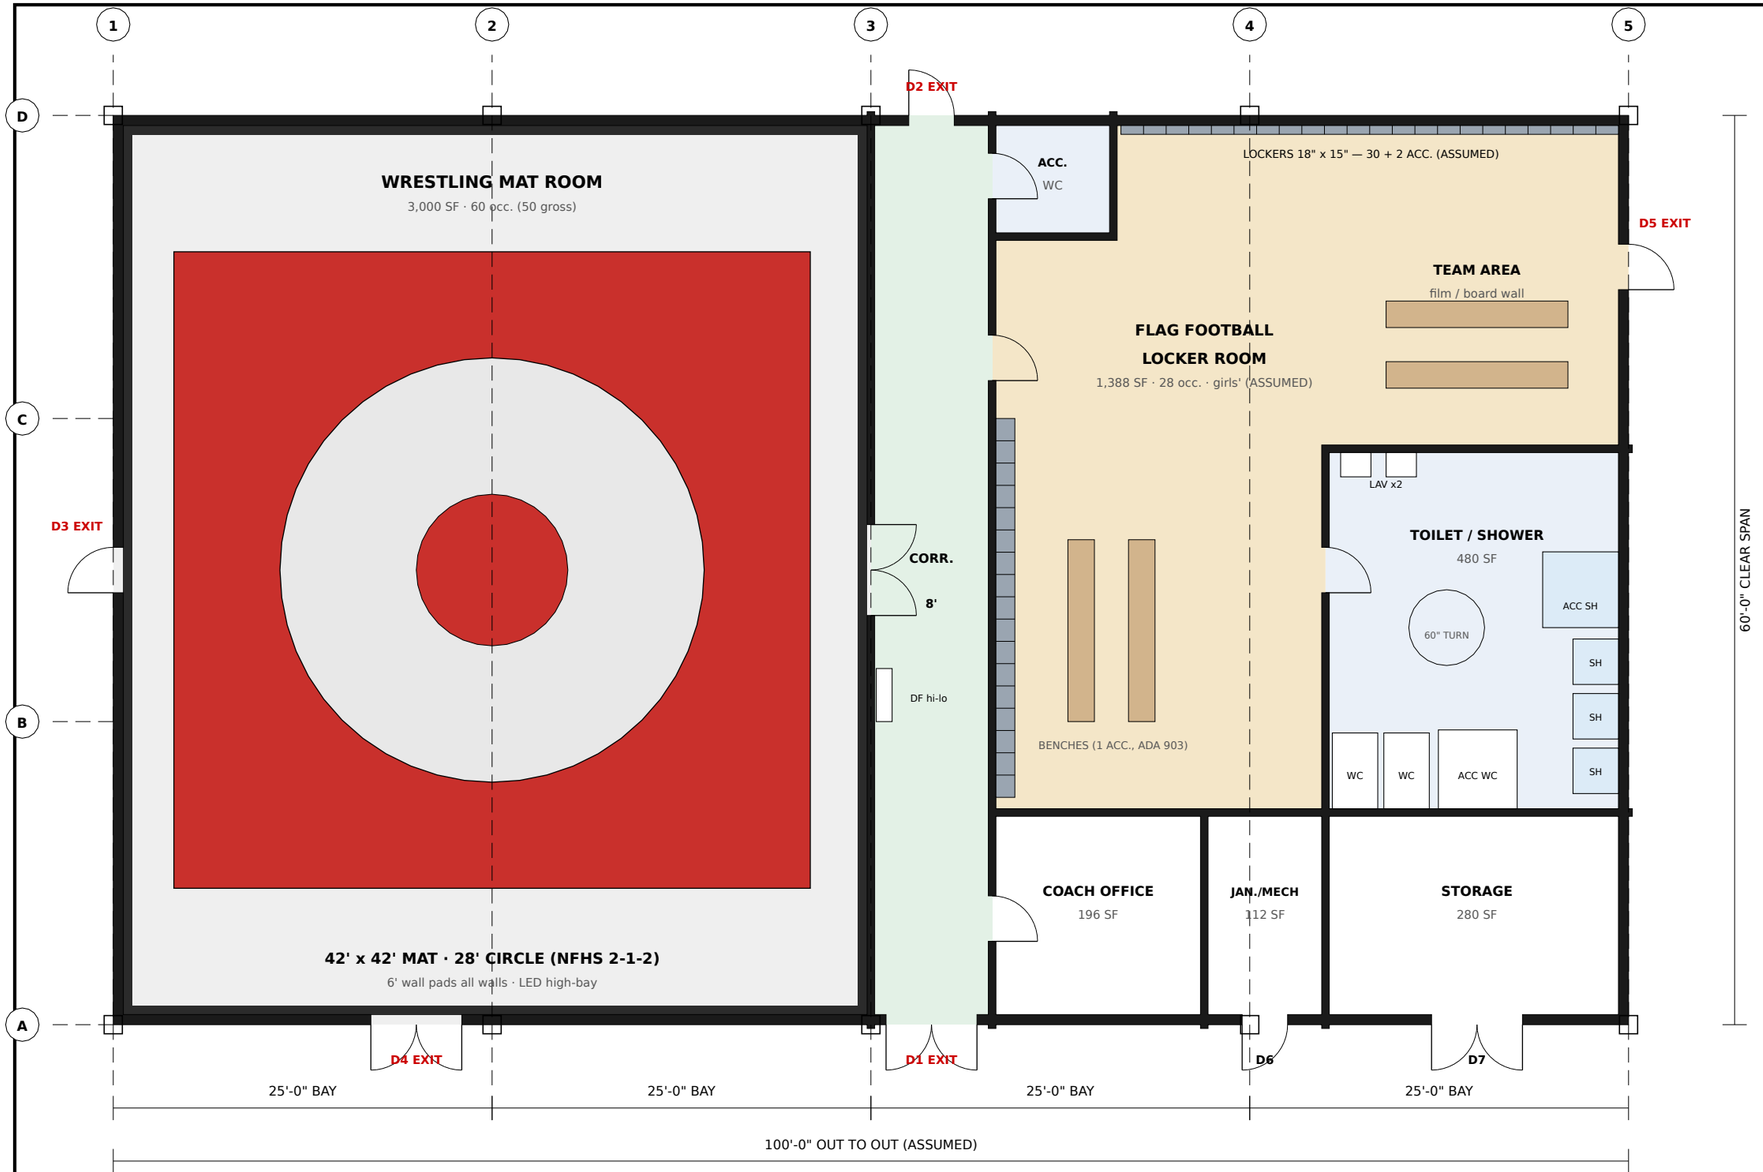

FLOOR PLAN — NEW METAL TRAINING BUILDING (ALTERNATE)

1" = 10'-0" · 100' x 60' = 6,000 SF clear-span PEMB, 4 x 25' bays (ASSUMED) · plan north up

PLAN NOTES


- D-094 (Shane 2026-10-14 9:52 PM CT): new pre-engineered metal building (Summertown Metals) replaces the old 55' x 45' room. West = mat room, east = flag football locker room.
- Size: the 60' x 80' alternate grown to 100' x 60' (ASSUMED) so the locker side holds toilets / showers, office and storage without shrinking the mat room.
- Clear-span rigid frames on lines 1-5 @ 25'; endwall columns @ 20' (A-D). Demising wall on line 3 (frame line). No interior columns.
- Mat room: one 42' x 42' mat (28' circle + 7' each side; NFHS 2-1-2 needs >= 5'). 4' E / W, 9' N / S to the walls; 6' wall pads all walls. Clear 14' min (ASSUMED).
- Locker room: girls' flag football (ASSUMED), 30 lockers + 2 accessible (ADA 222.1, 811), benches (ADA 903), team / film area.
- Toilet / shower: 3 WC (1 acc.), 2 lav, 4 showers (1 acc. roll-in). All-gender accessible single-user toilet off the corridor. DF hi-lo, service sink in JAN. (counts ASSUMED; G-101).
- Exits (red): D1 main pair, D2 north, D3 west, D4 mat-room pair, D5 east. Mat room (60 occ.) has 3 ways out (D3, D4, corridor I1).
- Accessibility: accessible route at grade, 60" turning spaces, 36" doors min; final ADA layout by the architect.
- Wall / interior: insulated metal panels (Summertown kit), 6" interior walls; wet walls TBD (CMU or moisture-resistant). Finishes TBD.
- No prices on this set: cost TBD per the Summertown Metals quote, plus site, foundation, MEP, permit and design (not included).

LEGEND


- wrestling mat (42' x 42')
- 6' wall pads
- locker room
- toilet / shower
- corridor / entry
- lockers

PRELIMINARY — CONCEPTUAL DESIGN — NOT FOR CONSTRUCTION


PROJECT	PHASE	SHEET TITLE	SCALE	DATE	REV	DRAWN BY	SHEET
Hazel Green Regional Athletic Complex **Hazel Green HS · Phase 1 alternate: new metal training building**	**PHASE 1 ALTERNATE**	**FLOOR PLAN** **METAL BUILDING (ALT.)**	**1" = 10'-0"**	**October 2026**	**A**	Drawn by KEYSTONE (AI) for Shane Brazelton	**P1-A-201**




SOUTH ELEVATION (MAIN ENTRY) — 1/16" = 1'-0"



EAST ELEVATION (LOCKER END) — 1/16" = 1'-0"



NORTH ELEVATION — 1/16" = 1'-0"



WEST ELEVATION (MAT ROOM END) — 1/16" = 1'-0"

SECTION A-A THROUGH THE MAT ROOM (looking west) — 1/10" = 1'-0"

NOTES


- Pre-engineered clear-span rigid frame, 1:12 gable (ASSUMED). Eave 16' (ASSUMED), ridge 18.50' computed from the pitch. Final frame, eave and clear height by Summertown Metals' engineer.
- Walls / roof: insulated metal panels (IMP or metal + liner, Summertown kit), R-values per the Alabama Energy Code (IECC 2015 / 90.1-2013) — TBD by supplier (R-028.4).
- Daylight: translucent wall-panel band 12'-14' (ASSUMED) on all faces; skylights only where code / supplier allow (D-093 direction). LED high-bay in the mat room; LED elsewhere.
- Color: crimson wainscot 0-3' (school color, ASSUMED); light gray panels; dark roof (ASSUMED). Gutters / downspouts to rain capture if the campus wants it (unsized).
- Doors: hollow-metal exit doors with panic hardware on D1-D5 (Group A, IBC 1010.2.9); D7 storage pair (not an exit). Red tags = exits.
- Foundation: slab-on-grade with column piers / anchor bolts per the PEMB reactions — geotech + structural TBD. No site plan yet (location on campus TBD).

PRELIMINARY — CONCEPTUAL DESIGN — NOT FOR CONSTRUCTION


PROJECT	PHASE	SHEET TITLE	SCALE	DATE	REV	DRAWN BY	SHEET
Hazel Green Regional Athletic Complex **Hazel Green HS · Phase 1 alternate: new metal training building**	**PHASE 1 ALTERNATE**	**ELEVATIONS + SECTION METAL BUILDING (ALT.)**	**1/16" = 1'-0"**	**October 2026**	**A**	Drawn by KEYSTONE (AI) for Shane Brazelton	**P1-A-301**

V1 AERIAL FROM THE SOUTHEAST (main entry + locker end)

isometric · not to scale · massing only

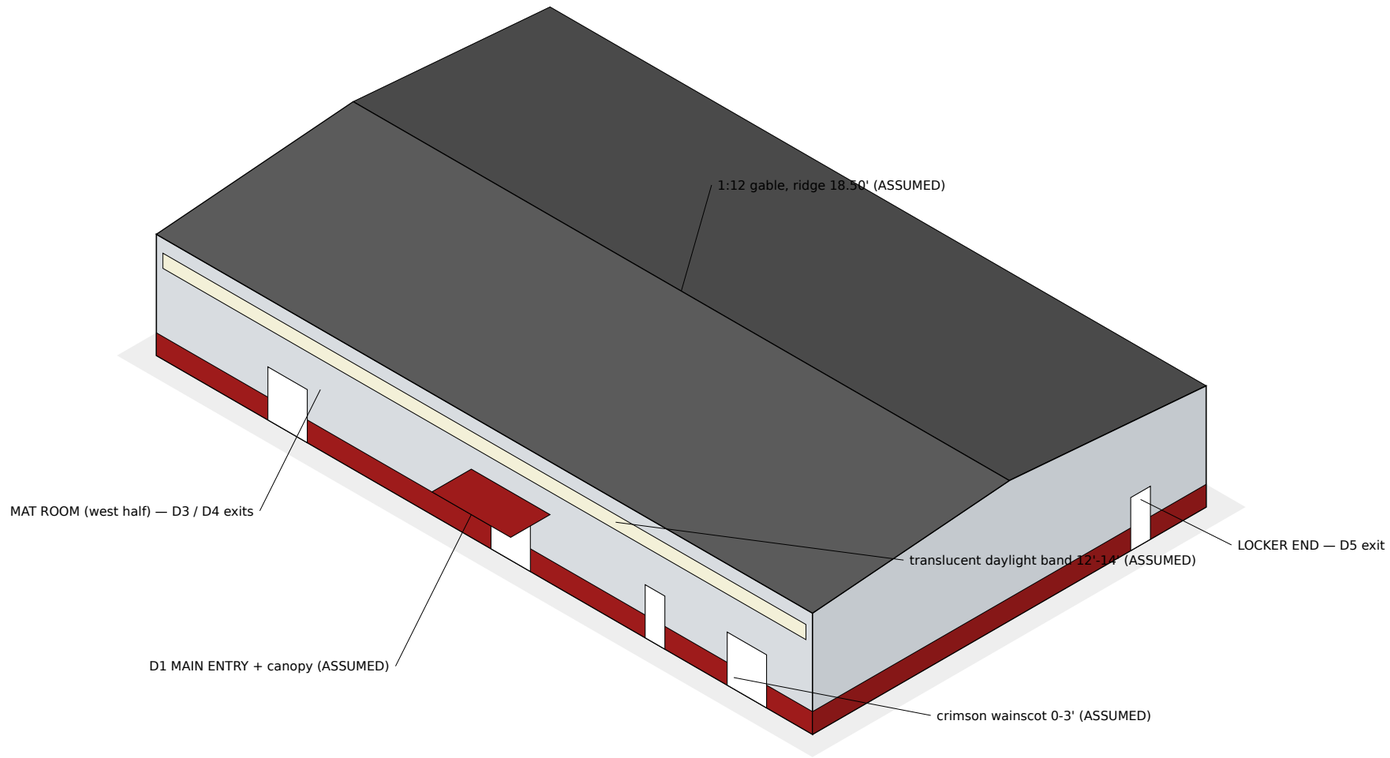

V2 FROM THE NORTHWEST (mat room end, D2 / D3)

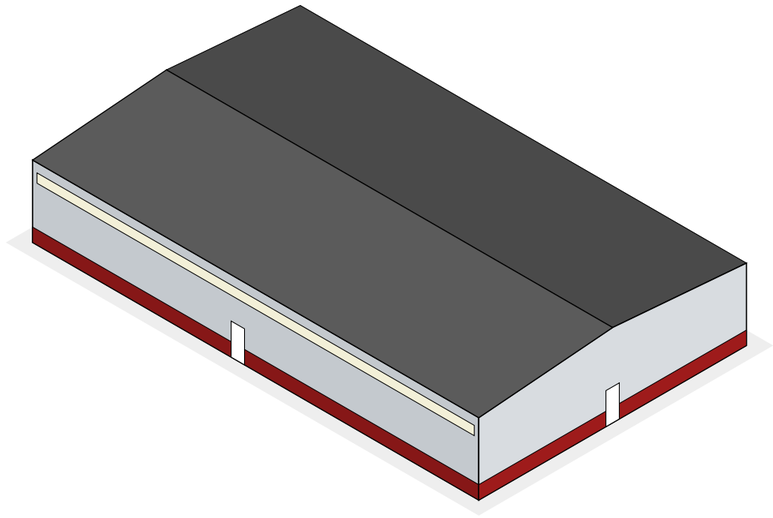

NOTES

- Massing only: 100' x 60' x 16' eave pre-engineered metal building (ASSUMED sizes) from params/phase1_metal_bldg.yaml.
- Summertown Metals kit (frame, panels, trim, doors). Colors, canopy and daylight band ASSUMED for discussion.
- Not modelled: site, grading, walks, parking, MEP units, gutters. Location on the HGHS campus TBD with Madison County Schools.
- Cost TBD per the supplier quote (no prices in this set).

PRELIMINARY — CONCEPTUAL DESIGN — NOT FOR CONSTRUCTION

PROJECT	PHASE	SHEET TITLE	SCALE	DATE	REV	DRAWN BY	SHEET
Hazel Green Regional Athletic Complex **Hazel Green HS · Phase 1 alternate: new metal training building**	**PHASE 1 ALTERNATE**	**3D MASSING** **METAL BUILDING (ALT.)**	**NTS**	**October 2026**	**A**	Drawn by KEYSTONE (AI) for Shane Brazelton	**P1-A-901**
